

Public Works June Monthly Report by Department

Ernesto Rios

Assistant/Interim PW Director

Plants Department

CITY OF LAGO VISTA WATER & WASTEWATER REPORT

June 2025



Water Production

This Month		Total Production - 47.281 MG				
	Raw Water	Production	Efficiency	Highest Day	Average Day	Lowest Day
Water Plant 1	-2.470 MG	18.580 MG	-752.1%	0.788 MG	0.619 MG	0.369 MG
Water Plant 2	0.000 MG	0.000 MG	∞%	--- MG	0.000 MG	--- MG
Water Plant 3	29.157 MG	28.701 MG	98.4%	1.355 MG	0.957 MG	0.600 MG
Combined	26.687 MG	47.281 MG	177.2%	2.092 MG	1.576 MG	1.007 MG

Past 12 Months		Total Production - 520.026 MG				
	Raw Water	Production	Efficiency	Highest Day	Average Day	Lowest Day
Water Plant 1	177.416 MG	186.037 MG	104.9%	0.845 MG	0.510 MG	0.091 MG
Water Plant 2	0.000 MG	0.000 MG	∞%	--- MG	0.000 MG	--- MG
Water Plant 3	338.458 MG	333.989 MG	98.7%	1.455 MG	0.915 MG	0.566 MG
Combined	515.874 MG	520.026 MG	100.8%	2.200 MG	1.425 MG	0.888 MG

Waste Water Treatment

This Month		Total Treated - 19.140 MG			
	Treated	Highest Day	Average Day	Lowest Day	
Waste Water Treatment Plant	19.140 MG	0.730 MG	0.638 MG	0.200 MG	

Past 12 Months		Total Treated - 212.496 MG			
	Treated	Highest Day	Average Day	Lowest Day	
Waste Water Treatment Plant	212.496 MG	0.820 MG	0.582 MG	0.200 MG	

Effluent Disposal


This Month		WWTP Plant Permit Total - 19.140 MG			
	Total	Highest Day	Average Day	Lowest Day	
Lago Vista Golf Course Permit	2.026 MG	0.121 MG	0.068 MG	0.020 MG	
Cedar Breaks Permit	23.196 MG	0.814 MG	0.773 MG	0.575 MG	
WWTP Plant Permit Total	19.140 MG	0.730 MG	0.638 MG	0.200 MG	
Reclaimed Effluent 210A Permit	0.000 MG	0.000 MG	0.000 MG	0.000 MG	

Past 12 Months		WWTP Plant Permit Total - 212.497 MG			
	Total	Highest Day	Average Day	Lowest Day	
Lago Vista Golf Course Permit	39.425 MG	0.359 MG	0.108 MG	0.000 MG	
Cedar Breaks Permit	208.166 MG	1.706 MG	0.570 MG	0.000 MG	
WWTP Plant Permit Total	212.497 MG	0.820 MG	0.582 MG	0.200 MG	
Reclaimed Effluent 210A Permit	0.000 MG	0.000 MG	0.000 MG	0.000 MG	

June 2025

Combined Water Production

This Month

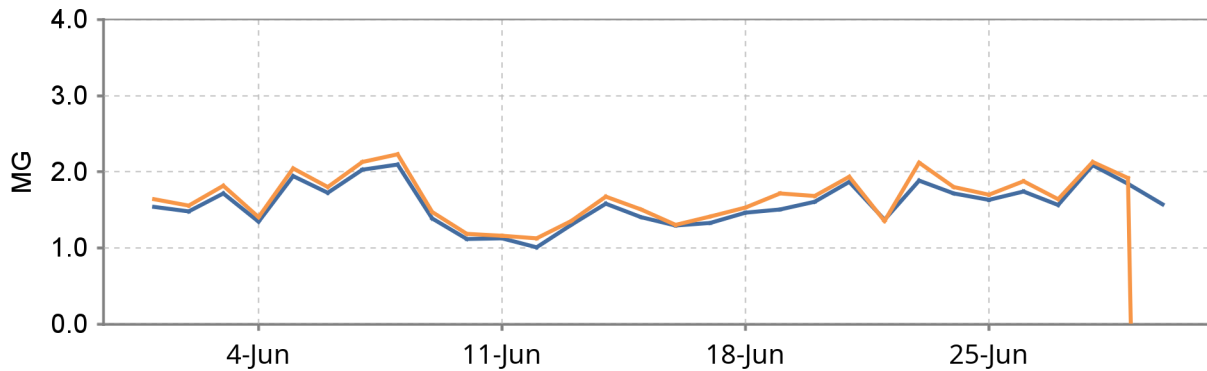


Date	WP1 Raw	WP2 Raw	WP3 Raw	Combined Raw	WP1 Finished	WP2 Finished	WP3 Finished	Combined Finished
06/01/25	0.684	---	0.956	1.639	0.604	---	0.936	1.540
06/02/25	0.633	---	0.925	1.558	0.576	---	0.904	1.480
06/03/25	0.645	---	1.176	1.821	0.593	---	1.127	1.720
06/04/25	0.833	---	0.575	1.408	0.744	---	0.600	1.345
06/05/25	0.843	---	1.200	2.043	0.758	---	1.190	1.948
06/06/25	0.724	---	1.081	1.805	0.635	---	1.093	1.728
06/07/25	0.843	---	1.284	2.127	0.788	---	1.241	2.029
06/08/25	0.843	---	1.391	2.234	0.737	---	1.355	2.092
06/09/25	0.424	---	1.046	1.469	0.369	---	1.022	1.391
06/10/25	0.452	---	0.734	1.186	0.419	---	0.696	1.114
06/11/25	0.483	---	0.676	1.159	0.429	---	0.696	1.125
06/12/25	0.452	---	0.670	1.122	0.389	---	0.618	1.007
06/13/25	0.503	---	0.854	1.357	0.453	---	0.847	1.299
06/14/25	0.712	---	0.961	1.673	0.644	---	0.938	1.582
06/15/25	0.632	---	0.878	1.509	0.553	---	0.853	1.407
06/16/25	0.574	---	0.731	1.305	0.524	---	0.767	1.291
06/17/25	0.644	---	0.766	1.410	0.554	---	0.775	1.330
06/18/25	0.742	---	0.790	1.532	0.668	---	0.798	1.465
06/19/25	0.662	---	1.058	1.720	0.612	---	0.896	1.507
06/20/25	0.703	---	0.980	1.682	0.604	---	1.004	1.608
06/21/25	0.815	---	1.124	1.940	0.738	---	1.127	1.865
06/22/25	0.623	---	0.729	1.352	0.544	---	0.830	1.374
06/23/25	0.853	---	1.266	2.119	0.760	---	1.122	1.882
06/24/25	0.772	---	1.032	1.804	0.669	---	1.047	1.715
06/25/25	0.793	---	0.908	1.702	0.730	---	0.904	1.634
06/26/25	0.803	---	1.076	1.879	0.701	---	1.037	1.738
06/27/25	0.623	---	1.013	1.637	0.562	---	1.001	1.564
06/28/25	0.853	---	1.274	2.127	0.777	---	1.309	2.086
06/29/25	0.813	---	1.107	1.920	0.717	---	1.124	1.841
06/30/25	-22.448	---	0.896	-21.552	0.728	---	0.844	1.572
Total (MG)	-2.470	0.000	29.157	26.687	18.580	0.000	28.701	47.281
Highest	0.853	---	1.391	2.234	0.788	---	1.355	2.092
Average	-0.082	0.000	0.972	0.890	0.619	0.000	0.957	1.576
Lowest	-22.448	---	0.575	-21.552	0.369	---	0.600	1.007


June 2025

Water Plant 1 Water Production

This Month

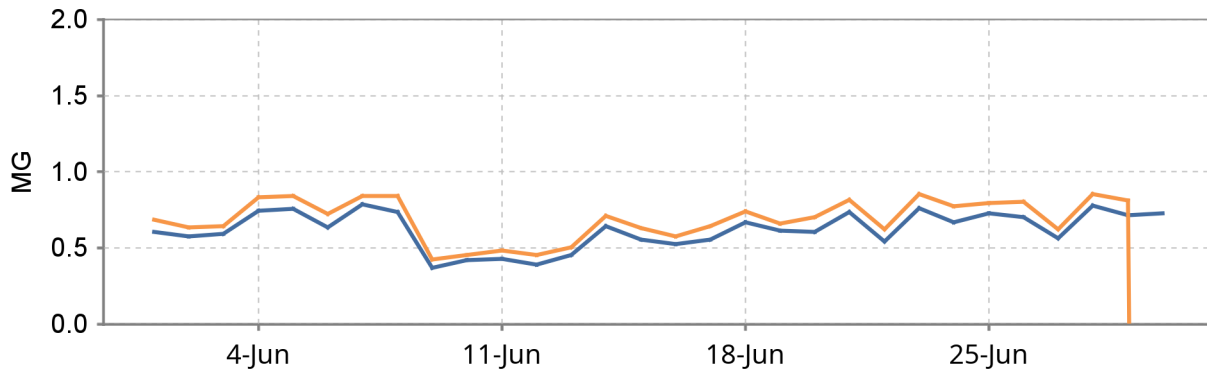


Date	WP1 Raw	WP1 Clarifier A	WP1 Clarifier B	WP1 Finished	WP1 Process Loss	WP1 Efficiency
06/01/25	0.684	0.000	0.684	0.604	0.079	88%
06/02/25	0.633	0.000	0.633	0.576	0.057	91%
06/03/25	0.645	0.000	0.645	0.593	0.052	92%
06/04/25	0.833	0.000	0.833	0.744	0.088	89%
06/05/25	0.843	0.000	0.843	0.758	0.084	90%
06/06/25	0.724	0.000	0.724	0.635	0.089	88%
06/07/25	0.843	0.000	0.843	0.788	0.056	93%
06/08/25	0.843	0.000	0.843	0.737	0.105	87%
06/09/25	0.424	0.000	0.424	0.369	0.055	87%
06/10/25	0.452	0.000	0.452	0.419	0.033	93%
06/11/25	0.483	0.000	0.483	0.429	0.054	89%
06/12/25	0.452	0.000	0.452	0.389	0.063	86%
06/13/25	0.503	0.000	0.503	0.453	0.050	90%
06/14/25	0.712	0.000	0.712	0.644	0.068	90%
06/15/25	0.632	0.000	0.632	0.553	0.078	88%
06/16/25	0.574	0.000	0.574	0.524	0.050	91%
06/17/25	0.644	0.000	0.644	0.554	0.089	86%
06/18/25	0.742	0.000	0.742	0.668	0.074	90%
06/19/25	0.662	0.000	0.662	0.612	0.050	92%
06/20/25	0.703	0.000	0.703	0.604	0.099	86%
06/21/25	0.815	0.000	0.815	0.738	0.077	91%
06/22/25	0.623	0.000	0.623	0.544	0.079	87%
06/23/25	0.853	0.000	0.853	0.760	0.092	89%
06/24/25	0.772	0.000	0.772	0.669	0.103	87%
06/25/25	0.793	0.000	0.793	0.730	0.064	92%
06/26/25	0.803	0.000	0.803	0.701	0.102	87%
06/27/25	0.623	0.000	0.623	0.562	0.061	90%
06/28/25	0.853	0.000	0.853	0.777	0.076	91%
06/29/25	0.813	0.000	0.813	0.717	0.096	88%
06/30/25	-22.448	0.000	-22.448	0.728	-23.176	-3%
Total (MG)	-2.470	0.000	-2.471	18.580	-21.050	-
Highest	0.853	0.000	0.853	0.788	-	-
Average	-0.082	0.000	-0.082	0.619	-	-752%
Lowest	-22.448	0.000	-22.448	0.369	-	-

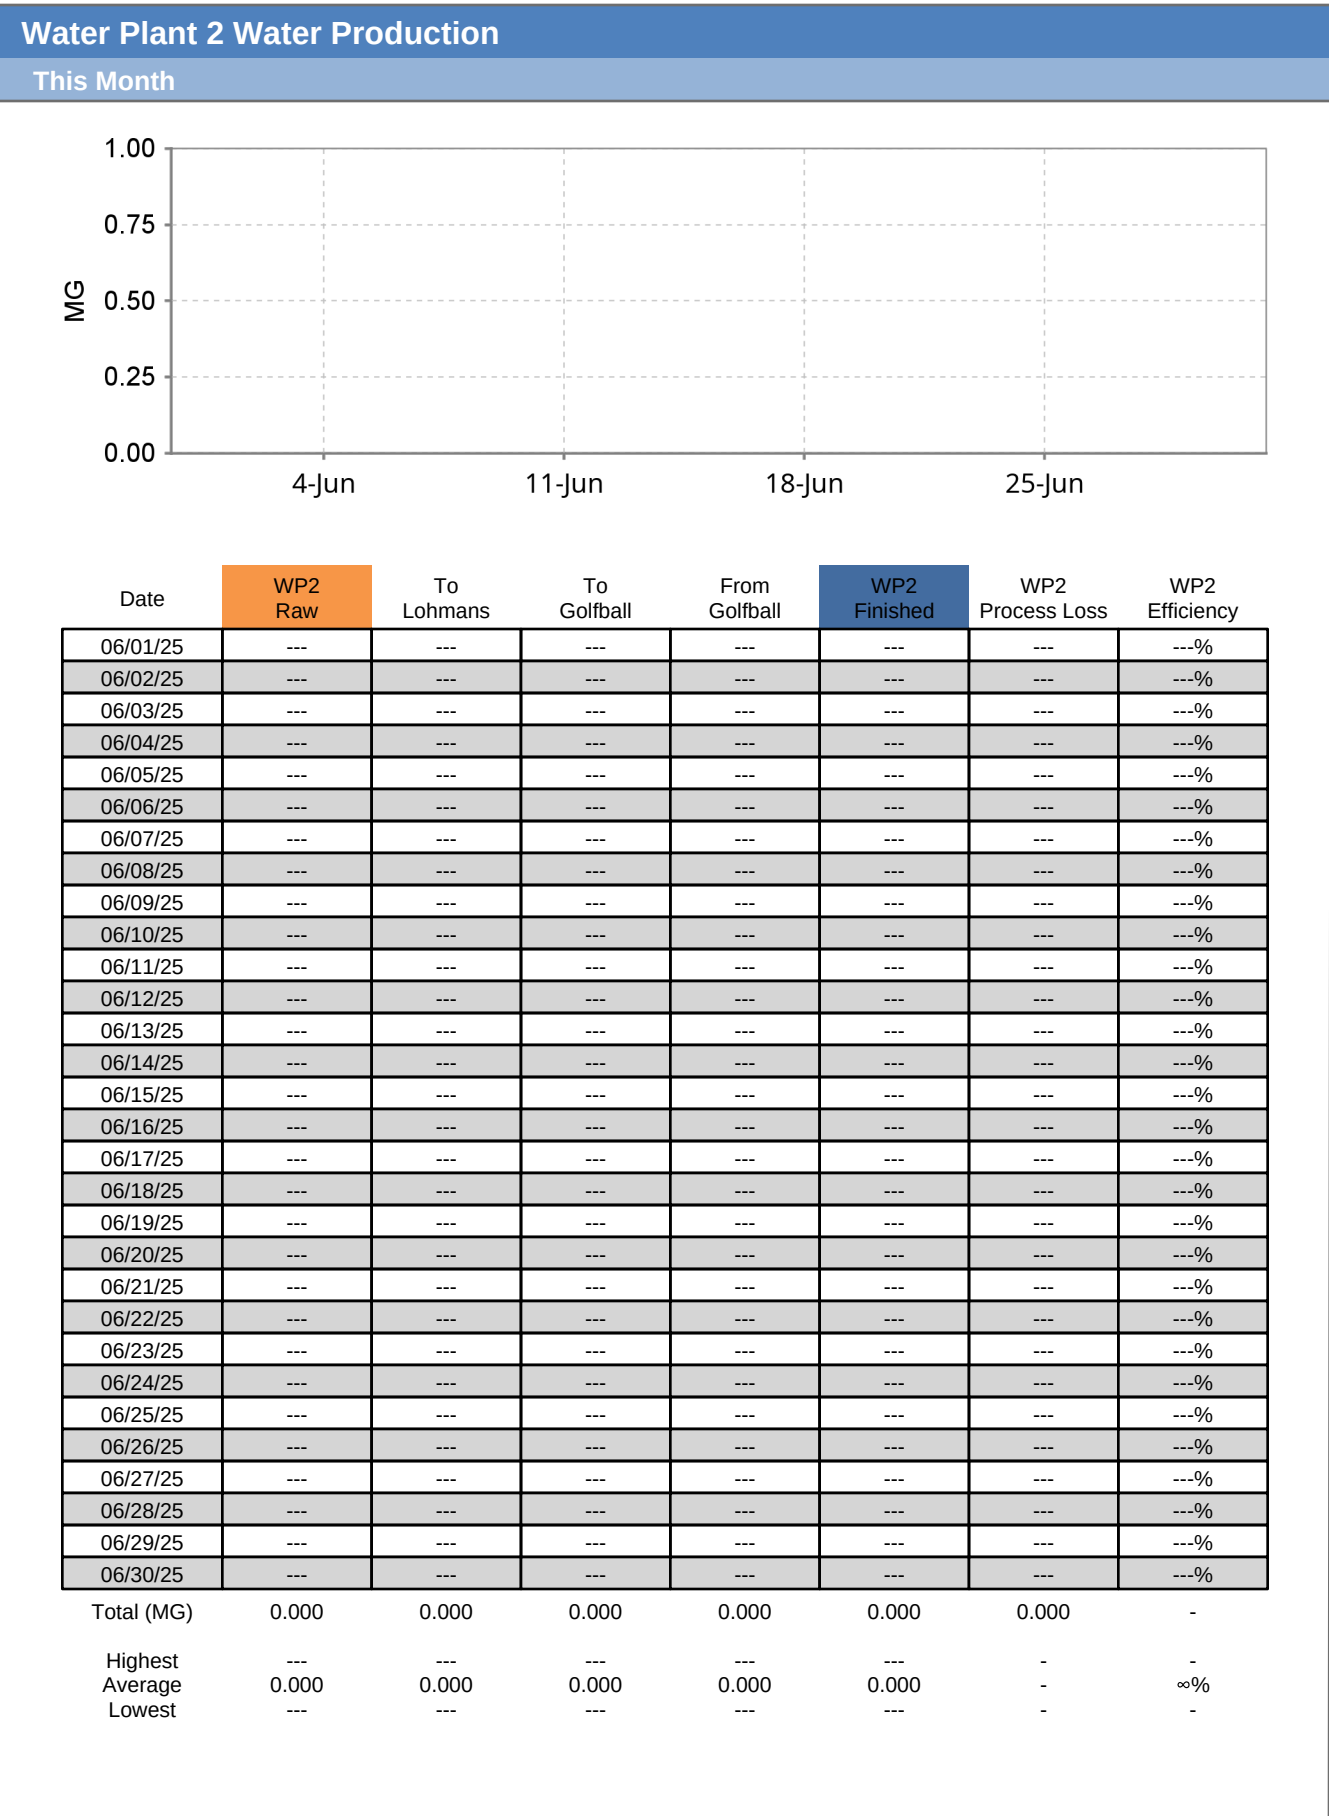

June 2025

Water Plant 3 Water Production

This Month

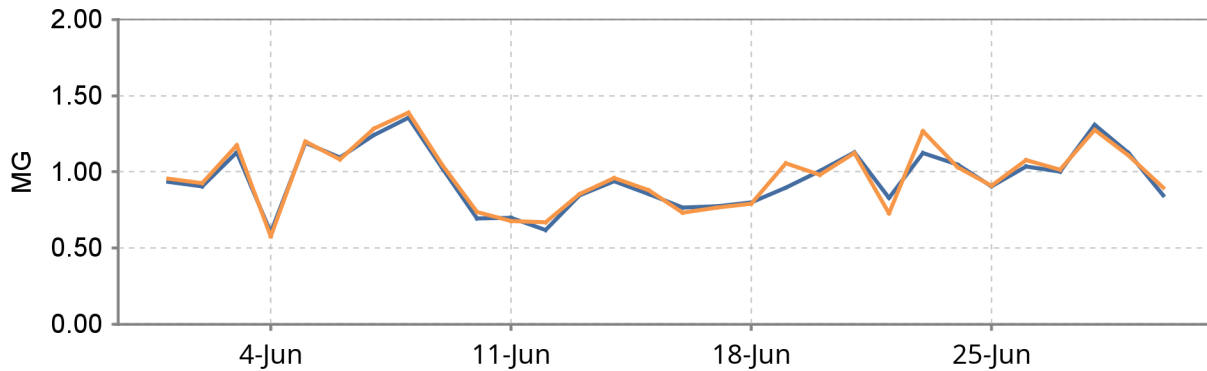


Date	WP3 Raw	WP3 Unit 1	WP3 Decant	WP3 Backwash	WP3 Finished	WP3 Process Loss	WP3 Efficiency
06/01/25	0.956	0.937	0.000	0.004	0.936	0.020	98%
06/02/25	0.925	0.968	0.000	0.051	0.904	0.021	98%
06/03/25	1.176	1.188	0.000	0.001	1.127	0.049	96%
06/04/25	0.575	0.636	0.000	0.052	0.600	-0.025	104%
06/05/25	1.200	1.200	0.000	0.003	1.190	0.011	99%
06/06/25	1.081	1.135	0.000	0.050	1.093	-0.012	101%
06/07/25	1.284	1.271	0.000	0.000	1.241	0.043	97%
06/08/25	1.391	1.458	0.000	0.052	1.355	0.036	97%
06/09/25	1.046	1.032	0.000	0.003	1.022	0.024	98%
06/10/25	0.734	0.791	0.000	0.049	0.696	0.039	95%
06/11/25	0.676	0.673	0.000	0.001	0.696	-0.020	103%
06/12/25	0.670	0.658	0.000	0.000	0.618	0.052	92%
06/13/25	0.854	0.938	0.000	0.049	0.847	0.007	99%
06/14/25	0.961	0.933	0.000	0.005	0.938	0.023	98%
06/15/25	0.878	0.944	0.000	0.053	0.853	0.024	97%
06/16/25	0.731	0.733	0.000	0.001	0.767	-0.036	105%
06/17/25	0.766	0.888	0.000	0.055	0.775	-0.009	101%
06/18/25	0.790	0.766	0.000	0.001	0.798	-0.007	101%
06/19/25	1.058	1.009	0.000	0.050	0.896	0.162	85%
06/20/25	0.980	0.967	0.000	0.002	1.004	-0.025	103%
06/21/25	1.124	1.158	0.000	0.050	1.127	-0.003	100%
06/22/25	0.729	0.755	0.000	0.006	0.830	-0.101	114%
06/23/25	1.266	1.350	0.000	0.047	1.122	0.144	89%
06/24/25	1.032	1.050	0.000	0.002	1.047	-0.015	101%
06/25/25	0.908	0.919	0.000	0.000	0.904	0.004	100%
06/26/25	1.076	1.121	0.000	0.055	1.037	0.039	96%
06/27/25	1.013	1.027	0.000	0.000	1.001	0.012	99%
06/28/25	1.274	1.340	0.000	0.049	1.309	-0.035	103%
06/29/25	1.107	1.158	0.000	0.055	1.124	-0.017	102%
06/30/25	0.896	0.913	0.000	0.002	0.844	0.052	94%
Total (MG)	29.157	29.916	0.000	0.748	28.701	0.456	-
Highest	1.391	1.458	0.000	0.055	1.355	-	-
Average	0.972	0.997	0.000	0.025	0.957	-	98%
Lowest	0.575	0.636	0.000	0.000	0.600	-	-

June 2025

Waste Water Treatment

This Month

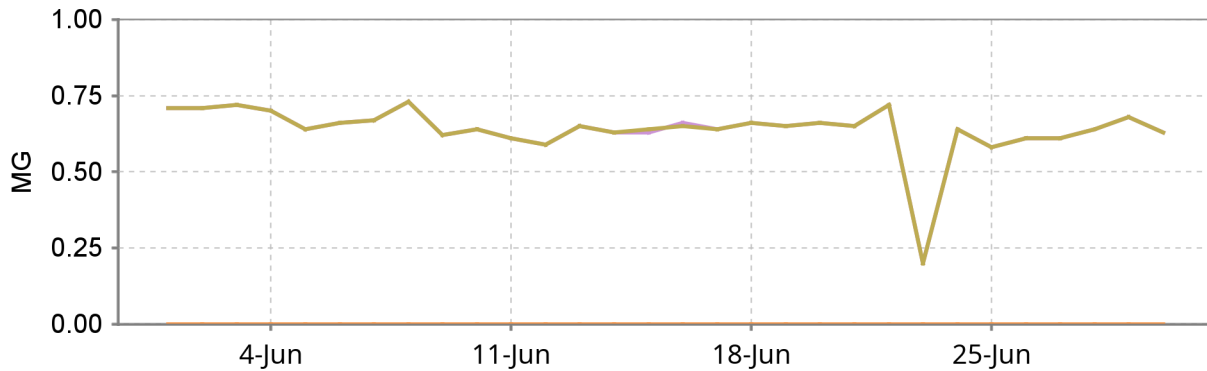


Date	WWTP Treated	LVGC Permit	Cedar Breaks Permit	WWTP Permit	Reclaimed Effluent 210A Permit
06/01/25	0.710	0.050	0.575	0.710	0.000
06/02/25	0.710	0.061	0.805	0.710	0.000
06/03/25	0.720	0.040	0.597	0.720	0.000
06/04/25	0.700	0.060	0.814	0.700	0.000
06/05/25	0.640	0.071	0.803	0.640	0.000
06/06/25	0.660	0.111	0.804	0.660	0.000
06/07/25	0.670	0.081	0.810	0.670	0.000
06/08/25	0.730	0.030	0.779	0.730	0.000
06/09/25	0.620	0.121	0.783	0.620	0.000
06/10/25	0.640	0.030	0.794	0.640	0.000
06/11/25	0.610	0.020	0.794	0.610	0.000
06/12/25	0.590	0.030	0.795	0.590	0.000
06/13/25	0.650	0.050	0.795	0.650	0.000
06/14/25	0.630	0.060	0.795	0.630	0.000
06/15/25	0.640	0.020	0.793	0.630	0.000
06/16/25	0.650	0.061	0.772	0.660	0.000
06/17/25	0.640	0.060	0.782	0.640	0.000
06/18/25	0.660	0.071	0.781	0.660	0.000
06/19/25	0.650	0.061	0.774	0.650	0.000
06/20/25	0.660	0.081	0.762	0.660	0.000
06/21/25	0.650	0.091	0.773	0.650	0.000
06/22/25	0.720	0.071	0.760	0.720	0.000
06/23/25	0.200	0.121	0.774	0.200	0.000
06/24/25	0.640	0.081	0.784	0.640	0.000
06/25/25	0.580	0.080	0.783	0.580	0.000
06/26/25	0.610	0.080	0.792	0.610	0.000
06/27/25	0.610	0.090	0.783	0.610	0.000
06/28/25	0.640	0.081	0.783	0.640	0.000
06/29/25	0.680	0.081	0.782	0.680	0.000
06/30/25	0.630	0.081	0.774	0.630	0.000
Total (MG)	19.140	2.026	23.196	19.140	0.000
Highest	0.730	0.121	0.814	0.730	0.000
Average	0.638	0.068	0.773	0.638	0.000
Lowest	0.200	0.020	0.575	0.200	0.000

June 2025

Effluent Disposal


This Month

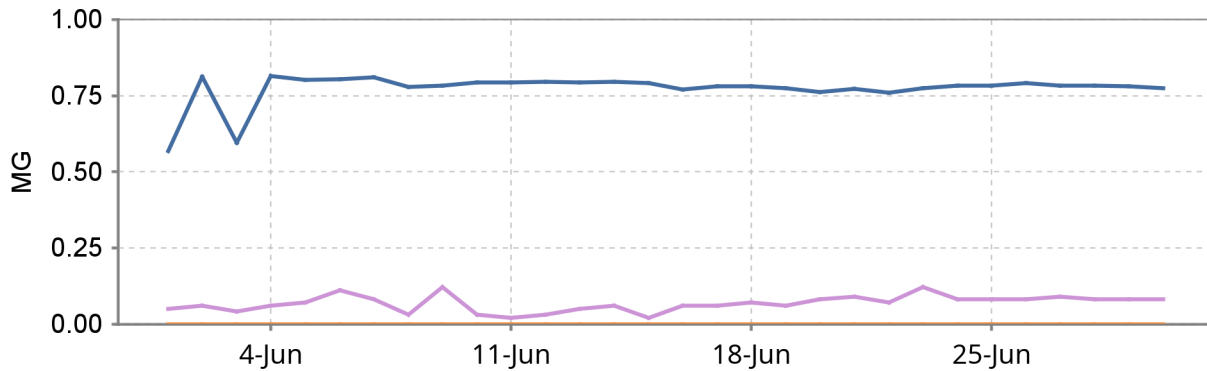


Date	LVGC Usage	LVGC Permit	Cedar Brks. Usage	Cedar Brks. Permit	HLGC Usage	Reclaimed E 210A Permit	LVGC Lake Water	HLGC Lake Water
06/01/25	0.050	0.050	0.569	0.575	0.000	0.000	0.000	---
06/02/25	0.061	0.061	0.813	0.805	0.000	0.000	0.000	---
06/03/25	0.040	0.040	0.596	0.597	0.000	0.000	0.000	---
06/04/25	0.060	0.060	0.814	0.814	0.000	0.000	0.000	---
06/05/25	0.071	0.071	0.803	0.803	0.000	0.000	0.000	---
06/06/25	0.111	0.111	0.804	0.804	0.000	0.000	0.000	---
06/07/25	0.081	0.081	0.810	0.810	0.000	0.000	0.000	---
06/08/25	0.030	0.030	0.779	0.779	0.000	0.000	0.000	---
06/09/25	0.121	0.121	0.783	0.783	0.000	0.000	0.000	---
06/10/25	0.030	0.030	0.794	0.794	0.000	0.000	0.000	---
06/11/25	0.020	0.020	0.794	0.794	0.000	0.000	0.000	---
06/12/25	0.030	0.030	0.795	0.795	0.000	0.000	0.000	---
06/13/25	0.050	0.050	0.795	0.795	0.000	0.000	0.000	---
06/14/25	0.060	0.060	0.795	0.795	0.000	0.000	0.000	---
06/15/25	0.020	0.020	0.793	0.793	0.000	0.000	0.000	---
06/16/25	0.061	0.061	0.772	0.772	0.000	0.000	0.000	---
06/17/25	0.060	0.060	0.782	0.782	0.000	0.000	0.000	---
06/18/25	0.071	0.071	0.781	0.781	0.000	0.000	0.000	---
06/19/25	0.061	0.061	0.774	0.774	0.000	0.000	0.000	---
06/20/25	0.081	0.081	0.762	0.762	0.000	0.000	0.000	---
06/21/25	0.091	0.091	0.773	0.773	0.000	0.000	0.000	---
06/22/25	0.071	0.071	0.760	0.760	0.000	0.000	0.000	---
06/23/25	0.121	0.121	0.774	0.774	0.000	0.000	0.000	---
06/24/25	0.081	0.081	0.784	0.784	0.000	0.000	0.000	---
06/25/25	0.080	0.080	0.783	0.783	0.000	0.000	0.000	---
06/26/25	0.080	0.080	0.792	0.792	0.000	0.000	0.000	---
06/27/25	0.090	0.090	0.783	0.783	0.000	0.000	0.000	---
06/28/25	0.081	0.081	0.783	0.783	0.000	0.000	0.000	---
06/29/25	0.081	0.081	0.782	0.782	0.000	0.000	0.000	---
06/30/25	0.081	0.081	0.774	0.774	0.000	0.000	0.000	---
Total (MG)	2.026	2.026	23.196	23.196	0.000	0.000	0.000	0.000
Highest	0.121	0.121	0.814	0.814	0.000	0.000	0.000	---
Average	0.068	0.068	0.773	0.773	0.000	0.000	0.000	0.000
Lowest	0.020	0.020	0.569	0.575	0.000	0.000	0.000	---

Combined Water Production

Past 12 Months

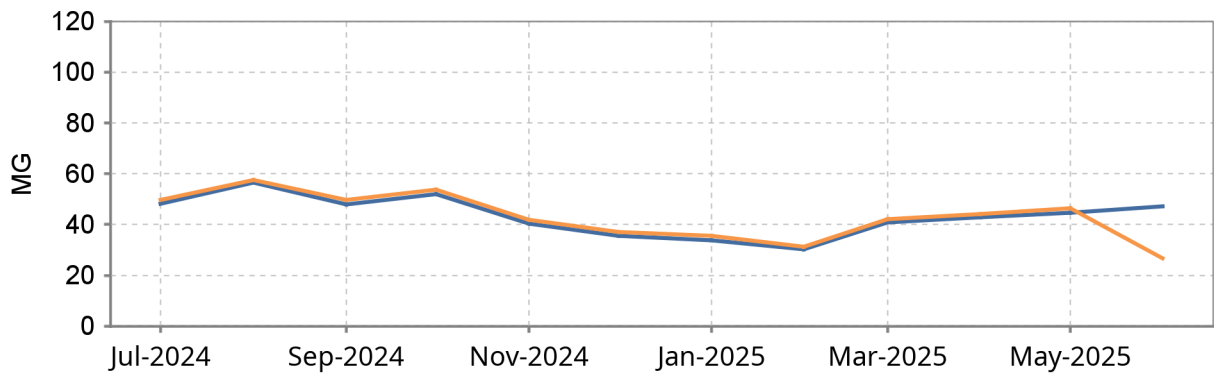


Date	WP1 Raw	WP2 Raw	WP3 Raw	Combined Raw	WP1 Finished	WP2 Finished	WP3 Finished	Combined Finished
Jul, 2024	18.856	---	30.889	49.745	17.765	---	30.557	48.322
Aug, 2024	21.790	---	35.757	57.547	21.129	---	35.392	56.521
Sep, 2024	21.205	---	28.396	49.601	19.761	---	28.103	47.864
Oct, 2024	23.252	---	30.507	53.759	21.669	---	30.228	51.897
Nov, 2024	17.782	---	23.999	41.782	16.545	---	23.802	40.347
Dec, 2024	15.482	---	21.496	36.978	14.160	---	21.328	35.489
Jan, 2025	11.775	---	23.728	35.503	10.690	---	23.098	33.788
Feb, 2025	8.754	---	22.587	31.341	7.994	---	22.296	30.290
Mar, 2025	12.710	---	29.489	42.199	11.754	---	29.025	40.779
Apr, 2025	11.366	---	32.828	44.194	10.450	---	32.365	42.815
May, 2025	16.914	---	29.624	46.538	15.540	---	29.093	44.633
Jun, 2025	-2.470	---	29.157	26.687	18.580	---	28.701	47.281
Total (MG)	177.416	0.000	338.458	515.874	186.037	0.000	333.989	520.026
Highest	23.252	---	35.757	57.547	21.669	---	35.392	56.521
Average	14.785	0.000	28.205	42.990	15.503	0.000	27.832	43.336
Lowest	-2.470	---	21.496	26.687	7.994	---	21.328	30.290

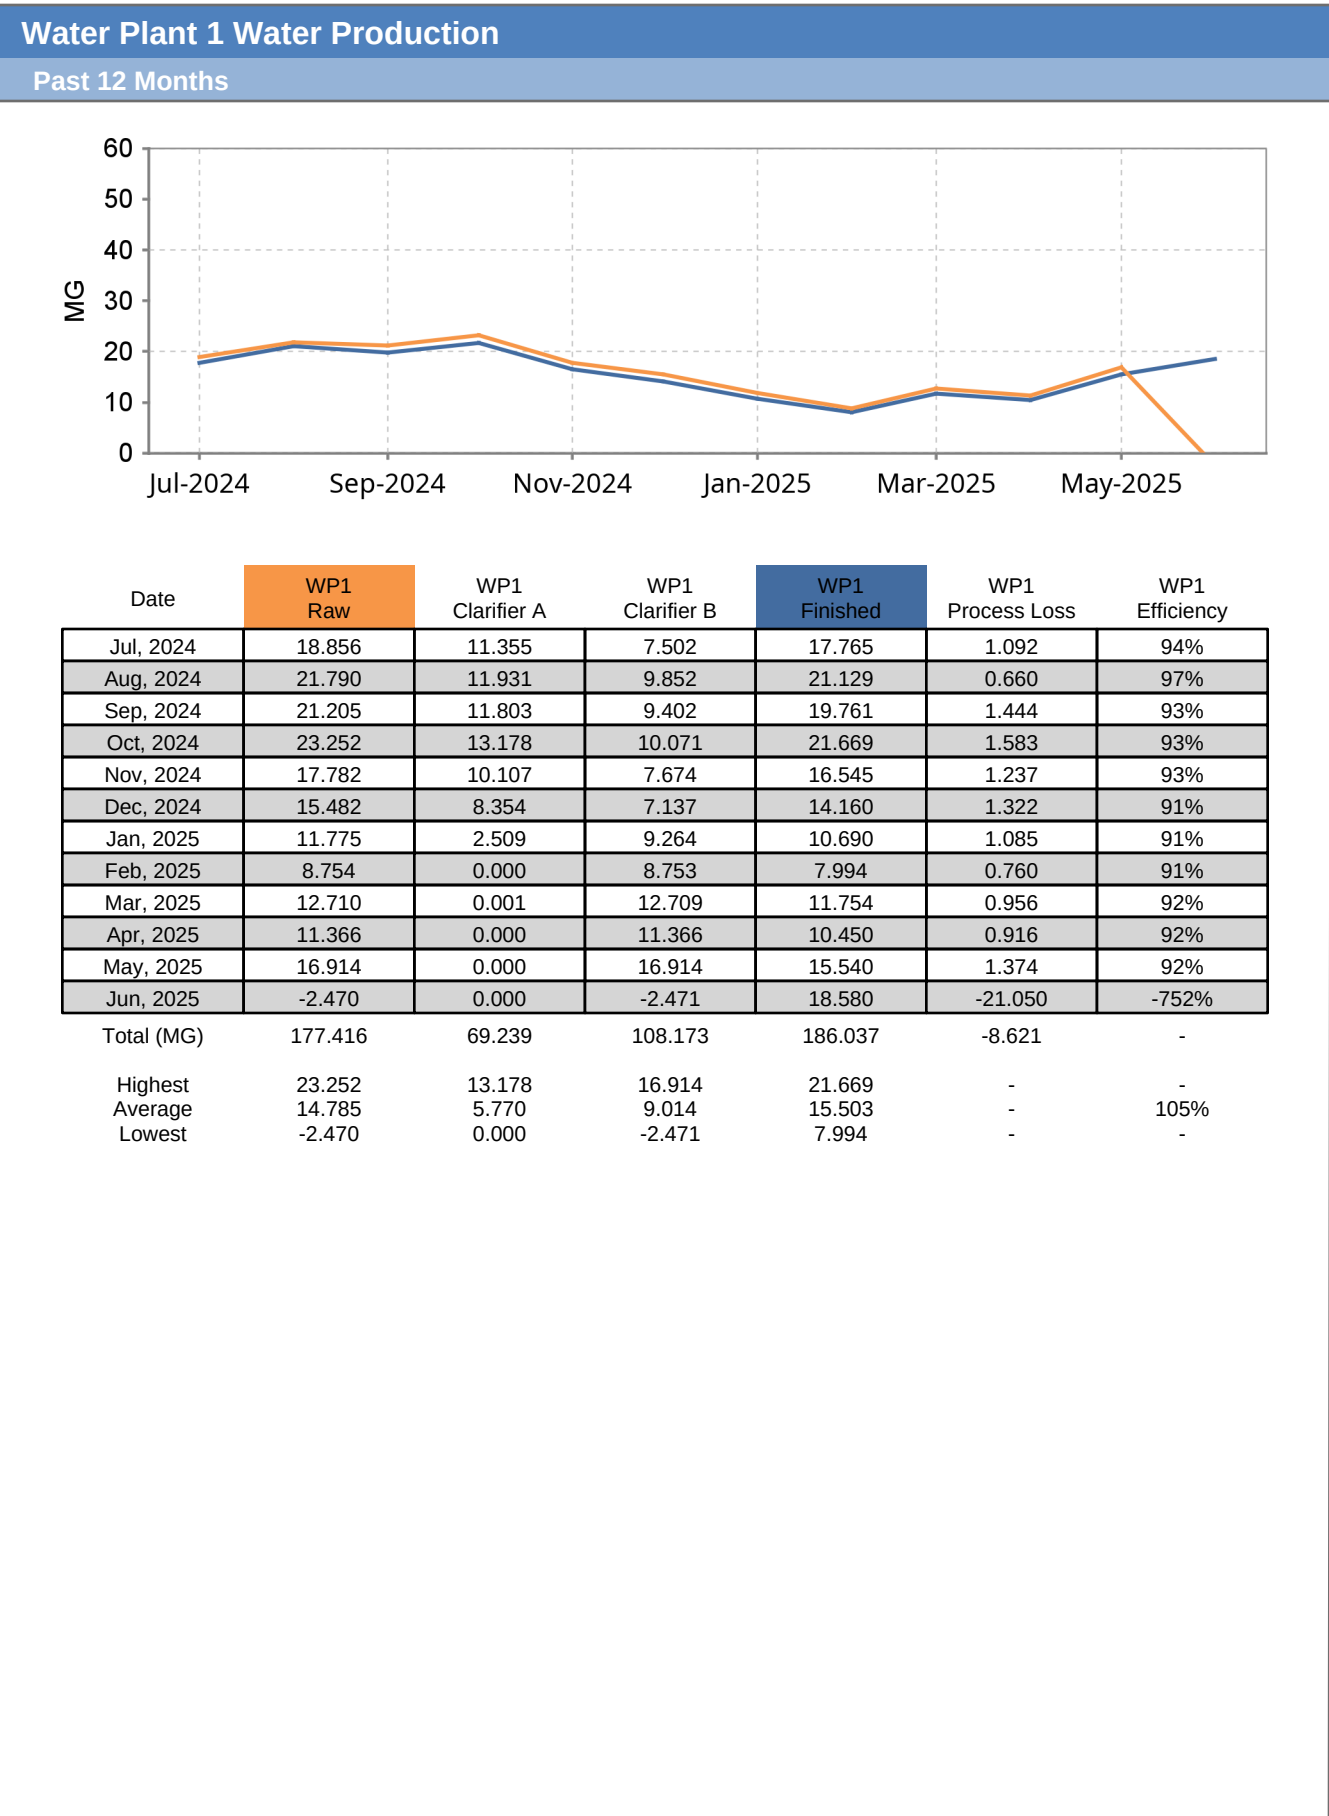

Water Plant 2 Water Production


Past 12 Months




Date	WP2 Raw	To Lohmans	To Golfball	From Golfball	WP2 Finished	WP2 Process Loss	WP2 Efficiency
Jul, 2024	---	---	---	---	---	---	---%
Aug, 2024	---	---	---	---	---	---	---%
Sep, 2024	---	---	---	---	---	---	---%
Oct, 2024	---	---	---	---	---	---	---%
Nov, 2024	---	---	---	---	---	---	---%
Dec, 2024	---	---	---	---	---	---	---%
Jan, 2025	---	---	---	---	---	---	---%
Feb, 2025	---	---	---	---	---	---	---%
Mar, 2025	---	---	---	---	---	---	---%
Apr, 2025	---	---	---	---	---	---	---%
May, 2025	---	---	---	---	---	---	---%
Jun, 2025	---	---	---	---	---	---	---%
Total (MG)	0.000	0.000	0.000	0.000	0.000	0.000	-
Highest	---	---	---	---	---	-	-
Average	0.000	0.000	0.000	0.000	0.000	-	∞%
Lowest	---	---	---	---	---	-	-

Water Plant 3 Water Production

Past 12 Months

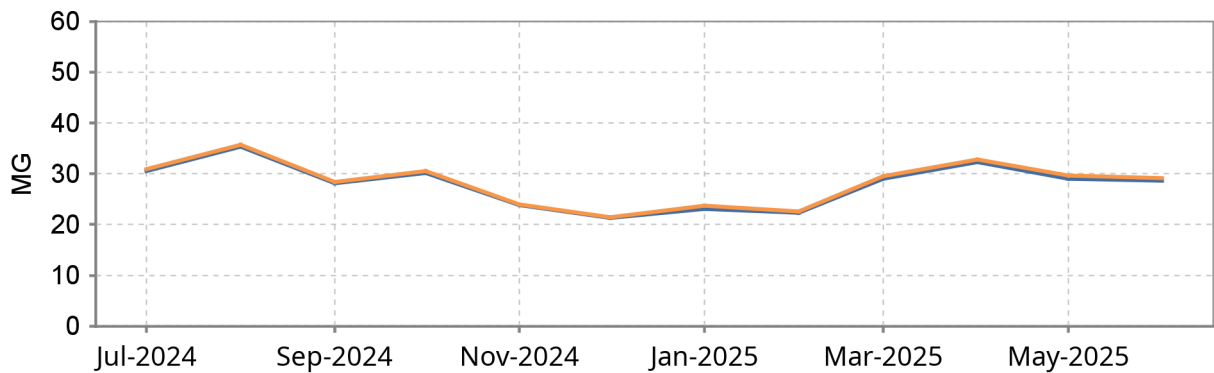


Date	WP3 Raw	WP3 Unit 1	WP3 Decant	WP3 Backwash	WP3 Finished	WP3 Process Loss	WP3 Efficiency
Jul, 2024	30.889	31.464	0.000	0.495	30.557	0.331	99%
Aug, 2024	35.757	36.729	0.000	0.768	35.392	0.365	99%
Sep, 2024	28.396	29.176	0.000	0.605	28.103	0.293	99%
Oct, 2024	30.507	31.274	0.000	0.656	30.228	0.279	99%
Nov, 2024	23.999	24.710	0.000	0.556	23.802	0.197	99%
Dec, 2024	21.496	22.048	0.000	0.422	21.328	0.168	99%
Jan, 2025	23.728	24.508	0.000	0.790	23.098	0.630	97%
Feb, 2025	22.587	23.460	0.000	0.816	22.296	0.291	99%
Mar, 2025	29.489	30.039	0.000	0.734	29.025	0.464	98%
Apr, 2025	32.828	33.456	0.000	0.740	32.365	0.463	99%
May, 2025	29.624	30.498	0.000	0.910	29.093	0.531	98%
Jun, 2025	29.157	29.916	0.000	0.748	28.701	0.456	98%
Total (MG)	338.458	347.279	0.000	8.241	333.989	4.469	-
Highest	35.757	36.729	0.000	0.910	35.392	-	-
Average	28.205	28.940	0.000	0.687	27.832	-	99%
Lowest	21.496	22.048	0.000	0.422	21.328	-	-

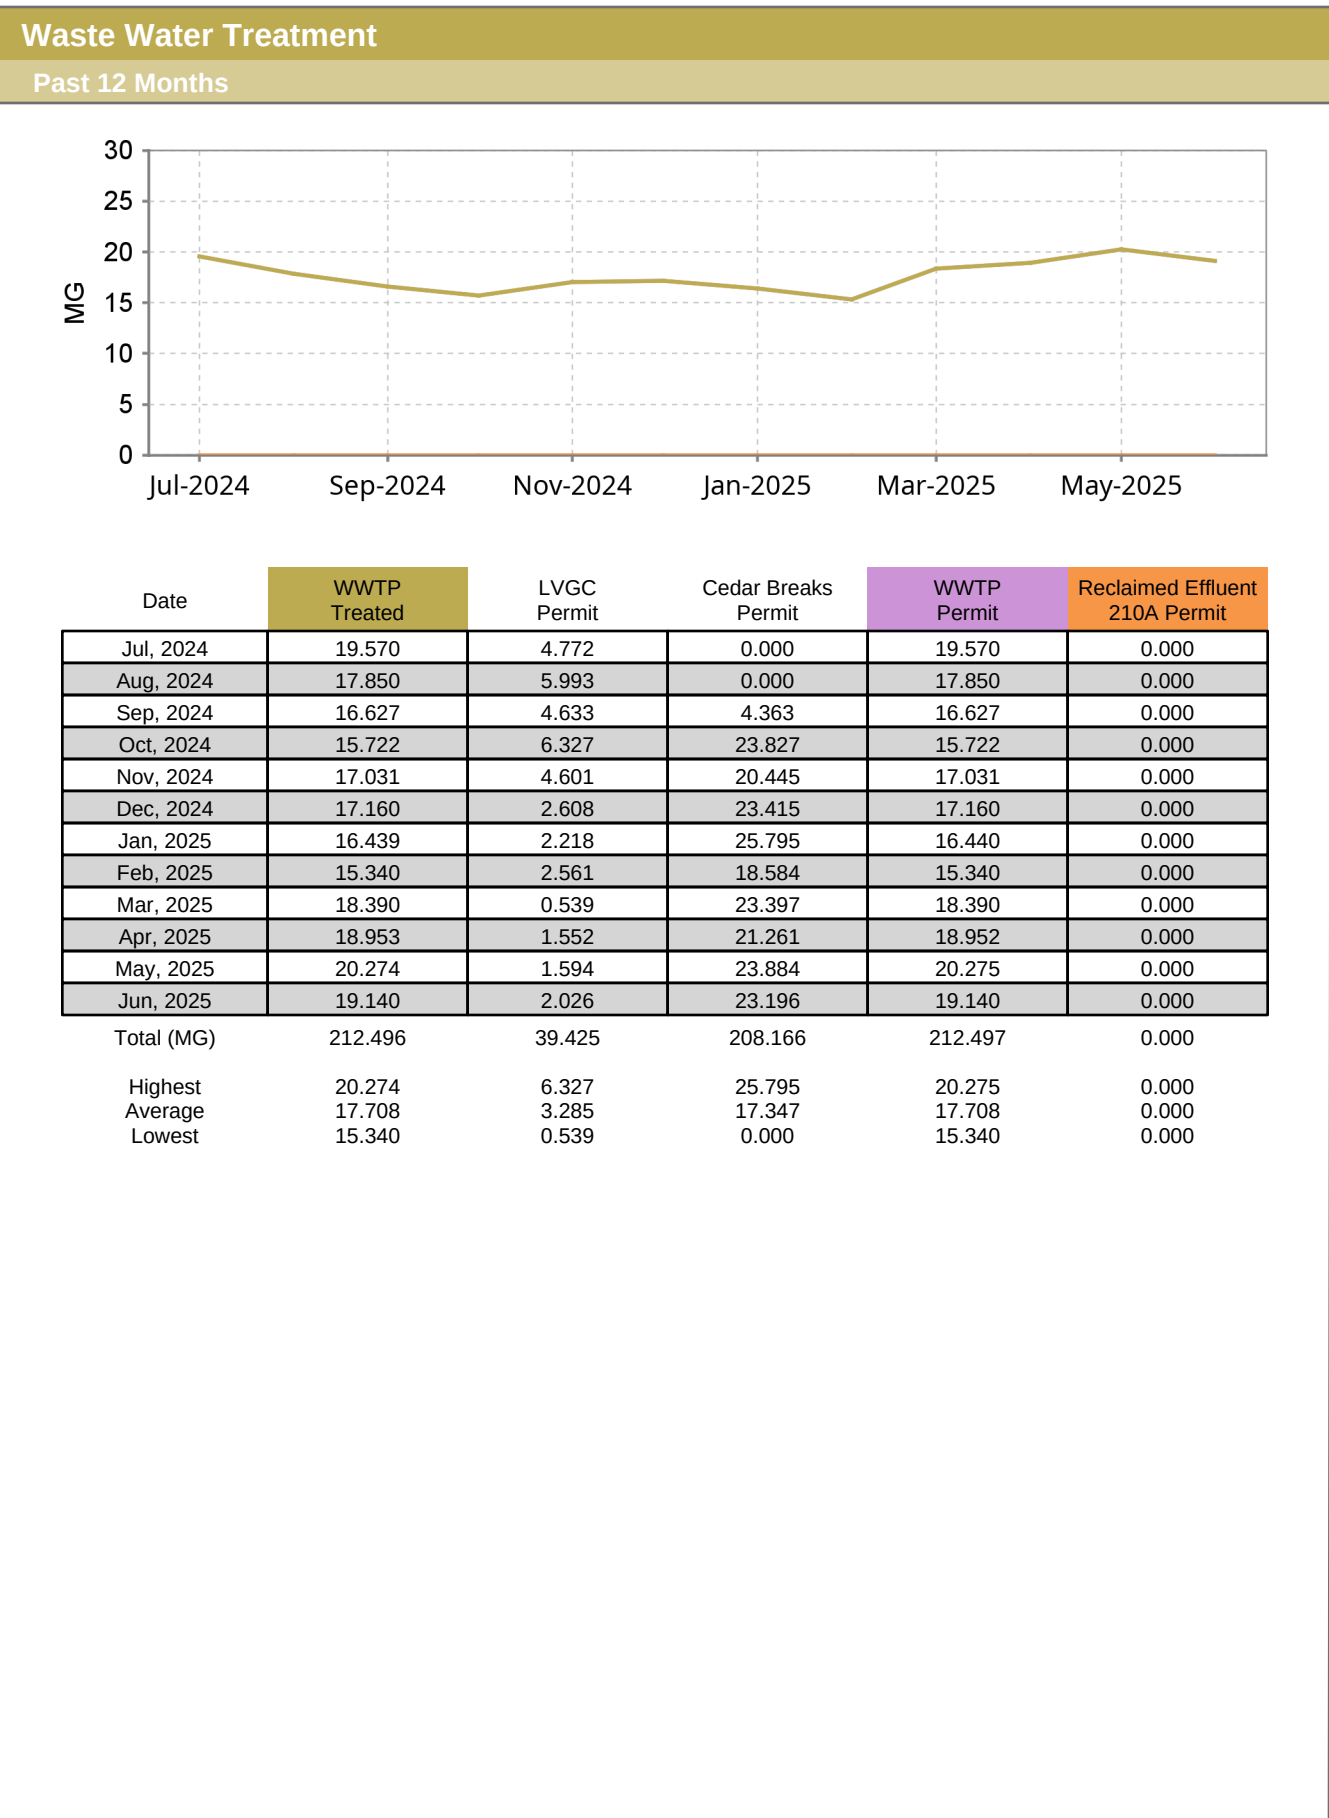

Effluent Disposal


Past 12 Months

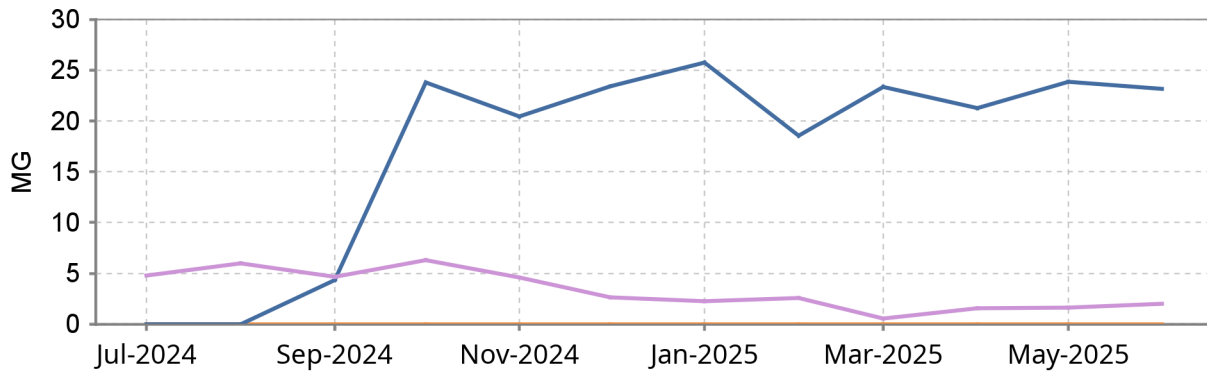

Date	LVGC Usage	LVGC Permit	Cedar Brks. Usage	Cedar Brks. Permit	HLGC Usage	Reclaimed E 210A Permit	LVGC Lake Water	HLGC Lake Water
Jul, 2024	4.772	4.772	0.000	0.000	0.000	0.000	0.000	---
Aug, 2024	5.993	5.993	0.000	0.000	0.000	0.000	0.000	---
Sep, 2024	4.633	4.633	4.363	4.363	0.000	0.000	0.000	---
Oct, 2024	6.327	6.327	23.827	23.827	0.000	0.000	0.000	---
Nov, 2024	4.601	4.601	20.445	20.445	0.000	0.000	0.000	---
Dec, 2024	2.605	2.608	23.415	23.415	0.000	0.000	0.000	---
Jan, 2025	2.221	2.218	25.795	25.795	0.000	0.000	0.000	---
Feb, 2025	2.561	2.561	18.584	18.584	0.000	0.000	0.000	---
Mar, 2025	0.539	0.539	23.397	23.397	0.000	0.000	0.000	---
Apr, 2025	1.552	1.552	21.261	21.261	0.000	0.000	0.000	---
May, 2025	1.594	1.594	23.884	23.884	0.000	0.000	0.000	---
Jun, 2025	2.026	2.026	23.196	23.196	0.000	0.000	0.000	---
Total (MG)	39.425	39.425	208.166	208.166	0.000	0.000	0.000	0.000
Highest	6.327	6.327	25.795	25.795	0.000	0.000	0.000	---
Average	3.285	3.285	17.347	17.347	0.000	0.000	0.000	0.000
Lowest	0.539	0.539	0.000	0.000	0.000	0.000	0.000	---

Combined Water Production


5 Year Average Daily Production

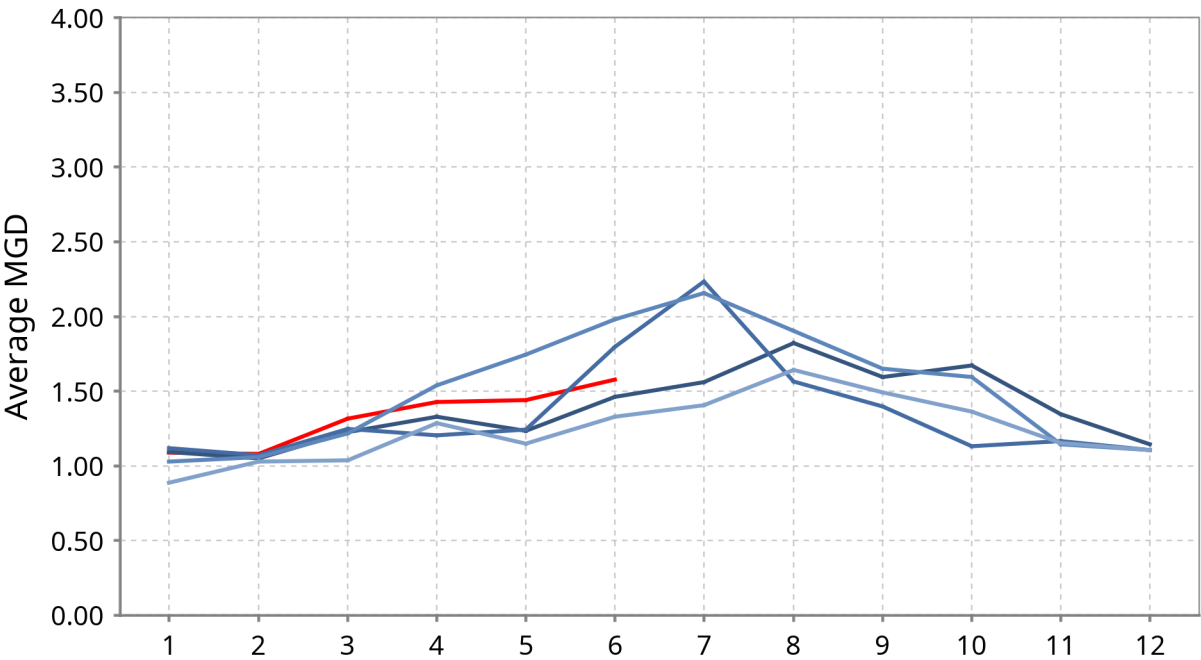

Month	Year - 4	Year - 3	Year - 2	Last Year	This Year
Jan	0.888	1.027	1.118	1.092	1.090
Feb	1.030	1.059	1.073	1.052	1.082
Mar	1.039	1.217	1.246	1.226	1.315
Apr	1.285	1.541	1.205	1.331	1.427
May	1.149	1.744	1.243	1.233	1.440
Jun	1.330	1.982	1.796	1.461	1.576
Jul	1.407	2.158	2.233	1.559	---
Aug	1.642	1.905	1.563	1.823	---
Sep	1.492	1.652	1.400	1.595	---
Oct	1.365	1.594	1.133	1.674	---
Nov	1.153	1.144	1.166	1.345	---
Dec	1.105	1.108	1.107	1.145	---
Highest	1.642	2.158	2.233	1.823	1.576
Average	1.240	1.511	1.357	1.378	1.322
Lowest	0.888	1.027	1.073	1.052	1.082

Waste Water Treatment

5 Year Average Daily Treated

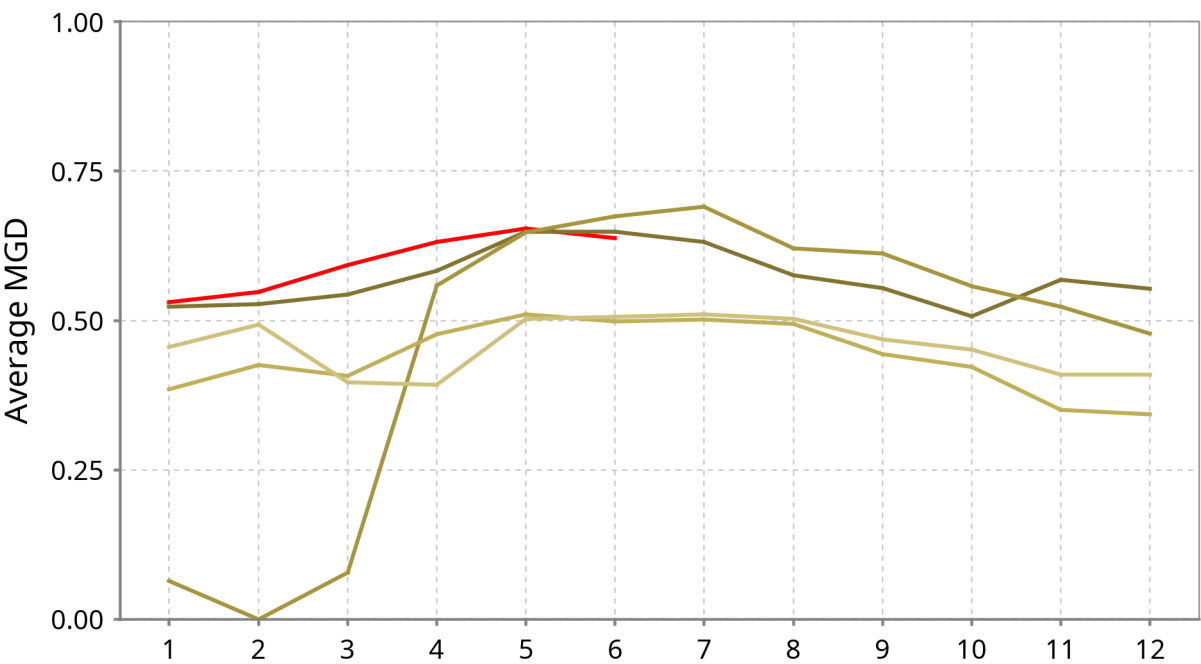

Month	Year - 4	Year - 3	Year - 2	Last Year	This Year
Jan	0.456	0.385	0.064	0.523	0.530
Feb	0.493	0.425	0.000	0.528	0.548
Mar	0.396	0.407	0.078	0.543	0.593
Apr	0.392	0.477	0.559	0.583	0.632
May	0.503	0.511	0.648	0.649	0.654
Jun	0.506	0.499	0.675	0.648	0.638
Jul	0.510	0.502	0.690	0.631	---
Aug	0.503	0.494	0.620	0.576	---
Sep	0.469	0.443	0.612	0.554	---
Oct	0.451	0.422	0.557	0.507	---
Nov	0.409	0.351	0.523	0.568	---
Dec	0.410	0.343	0.478	0.554	---
Highest	0.510	0.511	0.690	0.649	0.654
Average	0.458	0.438	0.459	0.572	0.599
Lowest	0.392	0.343	0.000	0.507	0.530

Utilities Department

June 2025 Field Crew and Fleet Maintenance Report

Field Crews Report

Five Sewer Service Installs
Three Drainage Repairs
Wastewater Plant Maintenance Project
Four Water Leak Repairs
One PRV installation
Three Suck Out Maintenance Repairs
One Water Service Install

Fleet Maintenance Report

Removed and Replaced Flap
Dropped off Truck for Special Repairs



Fleet Events By Date Range

Lago Vista

Date Range:

6/1/2025 - 6/30/2025

Date: 6/24/2025

Status: Complete

Assigned To: Joel Peer

Event ID: 7001

Event Type: Other

Work Order ID:

Feature ID: Mack Vac Truck

Feature Class: Fleet Unit

Fee:

Note: driver side rear most inner tire was off the bead and youngblood tire came out to reset it onto the rim .

Date: 6/10/2025

Status: Complete

Assigned To: Joel Peer

Event ID: Tensioner Replacement

Event Type: Service

Work Order ID:

Feature ID: Chevy Silverado Double
Cab Pickup

Feature Class: Fleet Unit

Fee:

Note: Truck was taken into Phonix automotive due to the repair needing a special tool.

Date: 6/24/2025

Status: Complete

Assigned To: Joel Peer

Event ID: 6016

Event Type: Other

Work Order ID:

Feature ID: 2022 Chevy Sliverado
5500 series

Feature Class: Fleet Unit

Fee:

Note: driver side mud flap removed and replaced

Total

3



Work Management Requests

Lago Vista

Date Range: 6/1/2025 - 6/30/2025

Start Date	End Date	Status	Request ID	Type	Sub Type	Assigned To
6/25/2025 12:00 AM	7/8/2025 12:00 AM	Complete	(SEWER SERVICE INSTALL) 21506 COYOTE TRL	Utilities	Other	Benjamin Moore
6/17/2025 12:00 AM	6/19/2025 12:00 AM	Complete	(DRAINAGE REPAIR) 3709 ROCK TERRACE DR	Utilities	Other	Benjamin Moore
6/16/2025 12:00 AM	6/17/2025 12:00 AM	Complete	(SEWER SERVICE ADJUSTMENT) 6914 CEDAR RIDGE DR	Utilities	Other	Benjamin Moore
6/12/2025 12:00 AM	6/19/2025 12:00 AM	Complete	(WASTEWATER PLANT PROJECT)	Utilities	Other	Benjamin Moore
6/10/2025 12:00 AM	6/17/2025 12:00 AM	Complete	(DRAINAGE ISSUE) 21514 PAINE AVE	Utilities	Other	Benjamin Moore
6/10/2025 12:00 AM	6/19/2025 12:00 AM	Complete	(DRAINAGE REPAIR) 2700 WILSON AVE	Utilities	Other	Benjamin Moore
6/9/2025 12:00 AM	6/10/2025 12:00 AM	Complete	(SEWER SERVICE INSTALL) 2600 WILSON AVE	Utilities	Other	Benjamin Moore
6/8/2025 12:00 AM	6/9/2025 12:00 AM	Complete	(WATER LEAK) 21601 SURREY LN	Utilities	Water Leak	Benjamin Moore
				Total	8	



Work Management Requests

Lago Vista

Date Range: 6/1/2025 - 6/30/2025

Start Date	End Date	Status	Request ID	Type	Sub Type	Assigned To
6/30/2025 12:00 AM	6/30/2025 12:00 AM	Complete	(CURBSTOP LEAK) 21431 COYOTE TRL	Utilities	Water Leak	Luis Mendoza
6/24/2025 12:00 AM	6/25/2025 12:00 AM	Complete	(SEWER SERVICE INSTALL) 7214 COMSTOCK CV	Utilities	Other	Luis Mendoza
6/23/2025 12:00 AM	7/10/2025 12:00 AM	Complete	(PRV Install) Wilson	Utilities	Other	Luis Mendoza
6/18/2025 12:00 AM	6/18/2025 12:00 AM	Complete	(SUCK OUT ISSUE) 21401 BULLET CV	Utilities	Other	Luis Mendoza
6/18/2025 12:00 AM	6/19/2025 12:00 AM	Complete	(WATER LEAK) 7303 WHITE OAK DR	Utilities	Other	Luis Mendoza
6/17/2025 12:00 AM	6/17/2025 12:00 AM	Complete	(SUCK OUT ISSUE) 21517 BISON TRL	Utilities	Other	Luis Mendoza
6/16/2025 12:00 AM	6/16/2025 12:00 AM	Complete	(SEWER SERVICE INSTALL) 21216 SANTA ROSA AVE	Utilities	Other	Luis Mendoza
6/16/2025 12:00 AM	6/17/2025 12:00 AM	Complete	(WATER SERVICE RELOCATION) 20301 CONTINENTAL DR	Utilities	Other	Luis Mendoza
6/16/2025 12:00 AM	6/16/2025 12:00 AM	Complete	(SUCK OUT ISSUE) 20617 FALCON	Utilities	Other	Luis Mendoza
6/14/2025 12:00 AM	6/14/2025 12:00 AM	Complete	(WATER LEAK) 21013 HIGHLAND LAKE DR	Utilities	Water Leak	Luis Mendoza
				Total	10	

Streets

Department

STREET DEPARTMENT WEEKLY ACTIVITY REPORT

2025 JUNE	WEEK 1	WEEK 2	WEEK 3	WEEK 4	TOTALS		
STREET PATCHING							
Tons of Asphatt Used							
Number of Patches							
Square Feet of Patches							
Tons of Base Material Used							
Repaint Intersections							
Replace Reflective Buttons							
CRACK SEAL PROGRAM							
Linear Feet of Crack Seating							
LANDSCAPING ACTIVITIES							
WorkerHours	12	13	20	20			65
ROADSIDE MOWING							
MilesMowed							
TRAFFIC CONTROL							
New Signs Installed	1	17	7	2			27
Signs Replaced				4			4
DRAINAGE MAINTENANCE							
Projects Completed							
Linear Feet of Drtches Cleared	890	450		180			1520
Culverts Cleared			5	2			7
MISCELLANEOUS ACTIVITIES							
Worker Hours on City Clean Up							
Worker Hours onBum Day							
Worker Hours onPark Maint.							
Worker Hours on X-Mas Lights							
Worker Hours on Tree Trimming							
Deer Pick Ups	3	2	4	1			10
Bldg. Maintenance Requests							
PoolOperation & Maintenance (hrs)							
Airport Maintenance (hrs)							
Mowing Bark Golf Course (hrs)							
Assist Utility Department (hrs)							
Assist CIP Projects (hrs)							
Assist Plant Operations (hrs)							
Assist Library (hrs)							
Assisi Effluent Department (hrs)							
Assist Golf Courses (hrs)							
Assist LVPD (hrs)							
KI VB Projects (hrs)							
Special Events (hrs)							
B!iiCYCb!; CENT!iIR							
Loads of Brush Collected		182					182
Wood Chipping (hrs)			22	30			52
Loads of Mulch Picked Up		28					28
Trash/Metal Collection (hrs)							
SPECIAL COMMENTS							
